


Activity ID	Activity Description	Successors	% Comp	Total Float	Orig Dur	Early Start	Early Finish	Late Finish	RESP	2005			
										MAY	JUN	JUL	AUG

MATOC RHODE ISLAND AIR NAT'L GUARD


Procurement Shop Drawings

A/E Approval										
1098	ShpDwg-SPECIALTIES	GM11416	0	18	20	20JUN05	18JUL05	11AUG05	SPEC	
1210	ShpDwg-DOORS/FRAMES/HARDWARE	1215*	0	0	20	20JUN05	18JUL05	18JUL05	DOOR	
1260	ShpDwg-GYPSUM BOARD SYSTEMS	GM11396*	0	12	20	20JUN05	18JUL05	03AUG05	GYP	
1270	ShpDwg-TILE	GM11412	0	20	20	20JUN05	18JUL05	15AUG05	TILEC	
1280	ShpDwg-ACOUSTICAL CEILINGS	GM11236	0	17	20	20JUN05	18JUL05	10AUG05	GYP	
1310	ShpDwg-PAINTING	GM11446	0	14	20	20JUN05	18JUL05	05AUG05	PAINT	
1320	ShpDwg-WALLCOVERING	GM11446	0	14	20	20JUN05	18JUL05	05AUG05	PAINT	
1340	ShpDwg-TOILET COMPARTMENTS	1345*	0	0	20	20JUN05	18JUL05	18JUL05	SPEC2	
1350	ShpDwg-LOUVERS/VENTS	1355*	0	7	20	20JUN05	18JUL05	27JUL05	LOCK	
1420	ShpDwg-TOILET/BATH ACCESSORIES	1425*	0	0	20	20JUN05	18JUL05	18JUL05	SPEC2	
1450	ShpDwg-MECHANICAL-INSULATION	GM11402	0	17	20	20JUN05	18JUL05	10AUG05	MECH	
1460	ShpDwg-MECHANICAL-PLUMBING FIXTURES	1465*	0	0	20	20JUN05	18JUL05	18JUL05	MECH	
1520	ShpDwg-MECH-FANS,CURBS	1525*	0	0	20	20JUN05	18JUL05	18JUL05	MECH	
1570	ShpDwg-ELECTRICAL-RACEWAYS	GM11278*	0	16	20	20JUN05	18JUL05	09AUG05	ELEC	
1580	ShpDwg-ELECTRICAL-WIRES/CABLES	GM11278*	0	16	20	20JUN05	18JUL05	09AUG05	ELEC	
1590	ShpDwg-ELECTRICAL-BOXES/FITTINGS	GM11278*	0	16	20	20JUN05	18JUL05	09AUG05	ELEC	
1600	ShpDwg-ELECTRICAL-WIRING DEVICES	GM11278*	0	16	20	20JUN05	18JUL05	09AUG05	ELEC	
1610	ShpDwg-ELECTRICAL-DISCONNECTS	GM11278*	0	16	20	20JUN05	18JUL05	09AUG05	ELEC	
1670	ShpDwg-ELECTRICAL-LIGHT FIXTURES	1675*	0	0	20	20JUN05	18JUL05	18JUL05	ELEC	

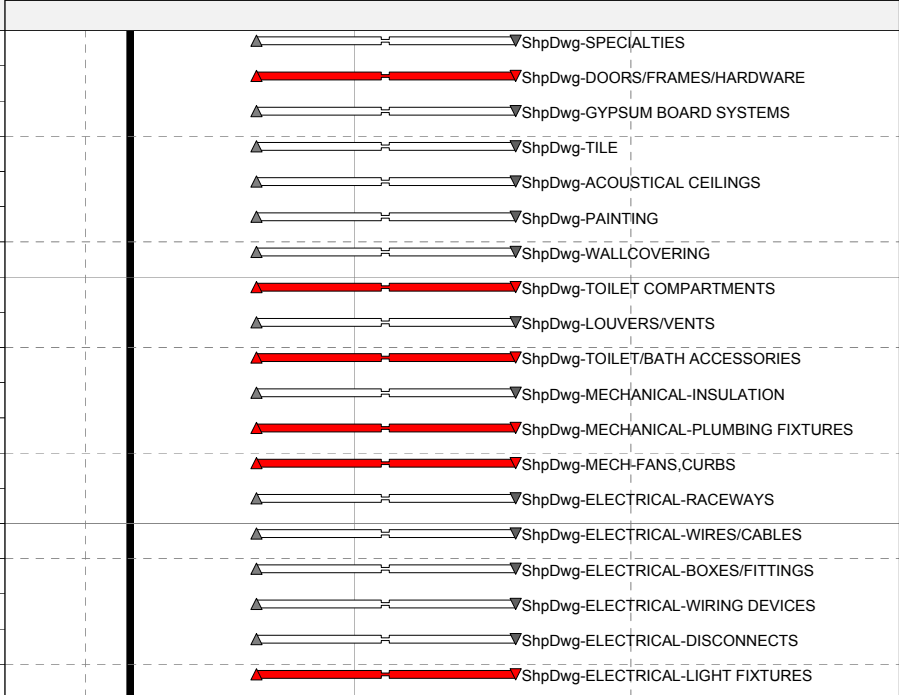


Procurement Fab/Delivery

Fabrication/Delivery										
1215	Fab-Doors/Frames/Hardware	GM11266*	0	0	18	19JUL05	11AUG05	11AUG05	DOOR	
1345	Fab-Toilet Compartments	GM11444*	0	0	18	19JUL05	11AUG05	11AUG05	SPEC2	
1355	Fab-Louvers/Vents	GM11364*, GM11365	0	7	10	19JUL05	01AUG05	10AUG05	MECH	
1425	Fab-Toilet/Bath Accessories	GM11442*	0	0	18	19JUL05	11AUG05	11AUG05	SPEC2	
1465	Fab-Plumbing Fixtures	GM11402*	0	0	17	19JUL05	10AUG05	10AUG05	MECH	
1525	Fab-Fans, Curbs, ETC.	GM11358*	0	0	18	19JUL05	11AUG05	11AUG05	MECH	
1675	Fab-Light Fixtures	GM11270*	0	0	19	19JUL05	12AUG05	12AUG05	ELEC	

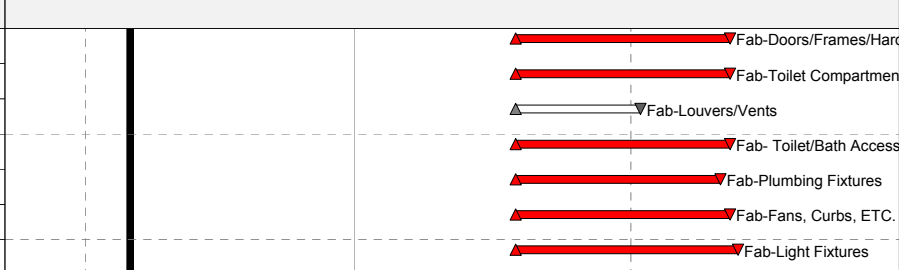

CONSTRUCTION PHASE: E-1: REPAIR RESTROOMS

GENERAL/ADMIN										
1790	AllPhase-Award Project Start	1098, 1210, 1260, 1270, 1280, 1310, 1320, 1340,	0	0	0	06JUN05			GEN	
1890	AllPhase-Stamped Plans	2440*, CLOSEOUT, THEEND	0	0	10	06JUN05	17JUN05	17JUN05	GEN	



Start Date: 06JUN05
 Finish Date: 17AUG05
 Data Date: 06JUN05
 Run Date: 26MAR05 05:14

▲ Early Bar
 ▼ Progress Bar
 ▲ Critical Activity

DCE1

Various Locations


Sheet 1 of 2

MATOC DC

Sol.: W912R1-05-R-0002 Exhibit E-1

Date	Revision	Checked	Approved

Activity ID	Activity Description	Successors	% Comp	Total Float	Orig Dur	Early Start	Early Finish	Late Finish	RESP				
										2005			
										MAY	JUN	JUL	AUG
1940	AllPhase-Permits/Fees/Notices	2440*, CLOSEOUT, THEEND	0	0	10	06JUN05	17JUN05	17JUN05	GEN				
2440	AllPhase-Notice to Proceed	1098*, 1210*, 1260*, 1270*, 1280*, 1310*	0	0	0	20JUN05			GEN				
2490	AllPhase-Mobilize	GM11310*	0	25	2	20JUN05	21JUN05	27JUL05	GEN				
2504	AllPhase-Bond/Insur./CPM/Shop Dwgs	GM11310	0	26	1	20JUN05	20JUN05	27JUL05	GEN				
2590	AllPhase-Layout	GM11310*	0	25	2	20JUN05	21JUN05	27JUL05	GEN				
CLOSEOUT	AllPhase-Project Closeout	THEEND*	0	0	1	17AUG05	17AUG05	17AUG05	GEN				
THEEND	AllPhase-PROJECT COMPLETION		0	0	0		17AUG05	17AUG05	GEN				

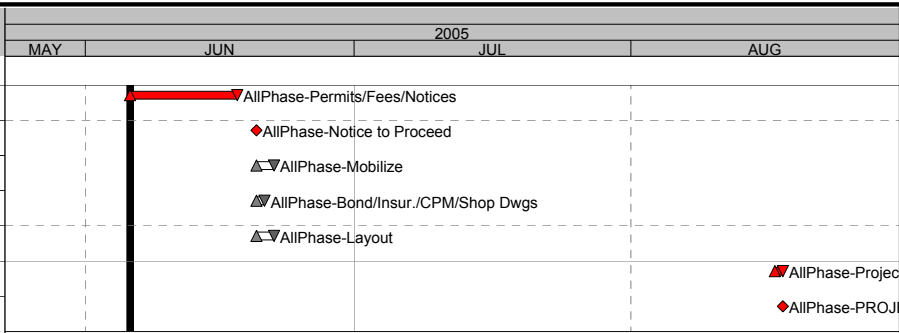

E-1: REPAIR CIVIL ENG. RESTROOMS - BLDG 3213

MAIN STRUCTURE									
GM11310	Main Build-Start	GM11278, GM11300*, GM11370, GM11396,	0	25	0	22JUN05			DEMO
GM11300	Main Build- General Demolition	GM11278, GM11316*, GM11364, GM11365,	0	25	3	24JUN05	28JUN05	03AUG05	GEN
GM11316	Main Build-Electrical Demolition	GM11278, GM11396, GM11412	0	27	1	24JUN05	24JUN05	03AUG05	ELEC
GM11418	Main Build-Plumb Demolition	GM11370*, GM11402	0	28	3	24JUN05	28JUN05	08AUG05	PLUMB
GM11370	Main Build-Mechanical RI	GM11364	0	28	2	29JUN05	30JUN05	10AUG05	MECH
GM11278	Main Build-Electrical RI	GM11270	0	16	3	19JUL05	21JUL05	12AUG05	ELEC
GM11396	Main Build-Metal Studs	GM11232*, GM11266, GM11330*, GM11358,	0	12	1	19JUL05	19JUL05	04AUG05	GYP
GM11232	Main Build-Carpentry/Blocking	GM11412	0	18	1	20JUL05	20JUL05	15AUG05	GEN
GM11330	Main Build-Gypsum Board	GM11236*, GM11268, GM11412, GM11446*	0	12	1	20JUL05	20JUL05	05AUG05	GYP
GM11236	Main Build-Ceiling Grid	GM11238, GM11270	0	15	1	21JUL05	21JUL05	11AUG05	GYP
GM11446	Main Build-Wall Covering/Paint	GM11238, GM11364, GM11402, GM11412,	0	12	3	21JUL05	25JUL05	10AUG05	PAINT
GM11416	Main Build-Specialties	GM11412	0	13	2	26JUL05	27JUL05	15AUG05	SPEC
GM11364	Main Build-Mechanical Finishes	GM11238*, GM11365	0	7	1	02AUG05	02AUG05	11AUG05	MECH
GM11238	Main Build-Ceiling Tile	GM11365, GM11412	0	7	1	03AUG05	03AUG05	12AUG05	GYP
GM11402	Main Build-Plumbing Finishes	GM11412*	0	0	3	11AUG05	15AUG05	15AUG05	PLUMB
GM11266	Main Build-Door Frames	GM11268*	0	0	1	12AUG05	12AUG05	12AUG05	DOOR
GM11358	Main Build-Mechanical Equipment	GM11365*, GM11412	0	0	1	12AUG05	12AUG05	12AUG05	MECH
GM11442	Main Build-Toilet Accessories	GM11412*	0	0	2	12AUG05	15AUG05	15AUG05	SPEC2
GM11444	Main Build-Toilet Partitions	GM11412*	0	0	2	12AUG05	15AUG05	15AUG05	SPEC2
GM11268	Main Build-Doors/Hardware	GM11412*	0	0	1	15AUG05	15AUG05	15AUG05	DOOR
GM11270	Main Build-Electrical Finishes	GM11412*	0	0	1	15AUG05	15AUG05	15AUG05	ELEC
GM11365	Main Build-Mechanical Test & Balance	GM11412*	0	0	1	15AUG05	15AUG05	15AUG05	MECH
GM11412	Main Build-Punchlist	CLOSEOUT*, THEEND	0	0	1	16AUG05	16AUG05	16AUG05	



Start Date	06JUN05	▲	▲	▼	Early Bar
Finish Date	17AUG05	▲	▲	▼	Progress Bar
Data Date	06JUN05	▲	▲	▼	Progress Bar
Run Date	26MAR05 05:14	▲	▲	▼	Critical Activity

DCE1 **Various Locations** Sheet 2 of 2
MATOC DC
Sol.: W912R1-05-R-002 Exhibit E-1

Date	Revision	Checked	Approved
