


Activity ID	Activity Description	% Comp	Total Float	Orig Dur	Early Start	Early Finish	Late Finish	RESP	2005				
									MAY	JUN	JUL	AUG	SEP

MATOC RHODE ISLAND AIR NAT'L GUARD

Procurement Shop Drawings

A/E Approval

Activity ID	Activity Description	% Comp	Total Float	Orig Dur	Early Start	Early Finish	Late Finish	RESP
1000	ShpDwg-RESTEEL DRAWINGS	0	9	20	20JUN05	18JUL05	29JUL05	RESTE
1010	ShpDwg-ANCHOR BOLT DRAWINGS	0	9	20	20JUN05	18JUL05	29JUL05	RESTE
1020	ShpDwg-CONCRETE MIX DESIGNS	0	14	20	20JUN05	18JUL05	05AUG05	GEN
1080	ShpDwg-LANDSCAPING	0	40	20	20JUN05	18JUL05	12SEP05	GEN
1100	ShpDwg-GUARD RAIL	0	16	20	20JUN05	18JUL05	09AUG05	STEEL
1200	ShpDwg-JOINT SEALANTS	0	35	20	20JUN05	18JUL05	05SEP05	GEN
1800	ShpDwg-RESTEEL/ANCHOR BOLT SHP DRWG	0	9	20	20JUN05	18JUL05	29JUL05	RESTE



Procurement Fab/Delivery

Fabrication/Delivery


Activity ID	Activity Description	% Comp	Total Float	Orig Dur	Early Start	Early Finish	Late Finish	RESP
1115	Fab-Guard Rail	0	16	15	19JUL05	08AUG05	30AUG05	STEEL
1118	Fab-Resteel	0	9	5	19JUL05	25JUL05	05AUG05	RESTE



CONSTRUCTION PHASE: E-3: BRIDGE RENOVATION

GENERAL/ADMIN


Activity ID	Activity Description	% Comp	Total Float	Orig Dur	Early Start	Early Finish	Late Finish	RESP
1790	AllPhase-Award Project Start	0	9	0	06JUN05			GEN
1890	AllPhase-Stamped Plans	0	9	10	06JUN05	17JUN05	30JUN05	GEN
1940	AllPhase-Permits/Fees/Notices	0	9	10	06JUN05	17JUN05	30JUN05	GEN
2440	AllPhase-Notice to Proceed	0	9	0	20JUN05			GEN
2490	AllPhase-Mobilize	0	25	5	20JUN05	24JUN05	01AUG05	GEN
2504	AllPhase-Bond/Insur./CPM/Shop Dwgs	0	29	1	20JUN05	20JUN05	01AUG05	GEN
2590	AllPhase-Layout	0	25	5	20JUN05	24JUN05	01AUG05	GEN
CLOSEOUT	AllPhase-Project Closeout	0	9	1	05SEP05	05SEP05	16SEP05	GEN
THEEND	AllPhase-PROJECT COMPLETION	0	9	0		05SEP05	16SEP05	GEN

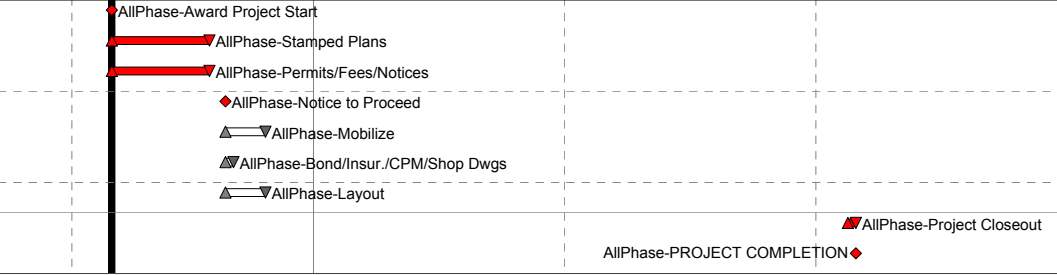

E-3: BRIDGE RENOVATION - BLDG 3029

SITE

Activity ID	Activity Description	% Comp	Total Float	Orig Dur	Early Start	Early Finish	Late Finish	RESP
G111746	Site-Start	0	25	0	27JUN05			GEN
G111744	Site-Silt Fencing/Alternate Path	0	25	3	28JUN05	30JUN05	05AUG05	GEN
G111710	Site-Earthwork/Site Prep	0	27	3	01JUL05	06JUL05	12AUG05	EARTH
G111756	Site-Concrete Footings	0	9	5	26JUL05	01AUG05	12AUG05	GEN
G111724	Site-Concrete Walls	0	9	12	02AUG05	17AUG05	30AUG05	GEN
G111741	Site-Parking Lot/Sidewalk	0	13	5	18AUG05	24AUG05	12SEP05	GEN
G111742	Site-Concrete Curb/Guard Rail	0	9	5	18AUG05	24AUG05	06SEP05	GEN
G111743	Site-Backfill and Grading	0	9	3	26AUG05	30AUG05	12SEP05	GEN
G111728	Site-Landscape/Striping	0	9	2	31AUG05	01SEP05	14SEP05	GEN
G111780	Site-Punchlist	0	9	1	02SEP05	02SEP05	15SEP05	GEN
G111781	Site-Completion	0	9	0		02SEP05	15SEP05	GEN

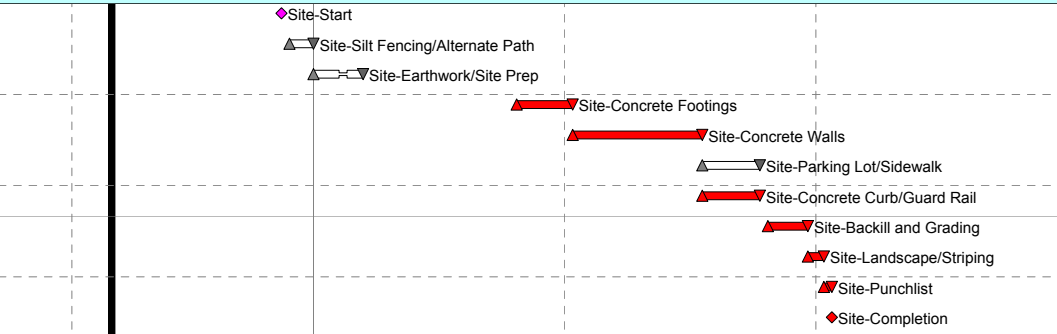

Start Date	06JUN05	▲	▼	Early Bar
Finish Date	05SEP05	▲	▼	Progress Bar
Data Date	06JUN05	▲	▼	Progress Bar
Run Date	26MAR05 05:15	▲	▼	Critical Activity

DCE3
Various Locations
 Sheet 1 of 1
MATOC DC
 Sol: W912R1-05-R-002 Exhibit E-3

Date	Revision	Checked	Approved
