


Activity ID	Activity Description	% Comp	Total Float	Orig Dur	Early Start	Early Finish	Late Finish	RESP	2005				
									MAY	JUN	JUL	AUG	SEP

# MATOC RHODE ISLAND AIR NAT'L GUARD

## Procurement Shop Drawings

### A/E Approval


1000	ShpDwg-RESTEEL DRAWINGS	0	30	20	20JUN05	18JUL05	29AUG05	RESTE
1010	ShpDwg-ANCHOR BOLT DRAWINGS	0	30	20	20JUN05	18JUL05	29AUG05	RESTE
1020	ShpDwg-CONCRETE MIX DESIGNS	0	10	20	20JUN05	18JUL05	01AUG05	GEN
1098	ShpDwg-SPECIALTIES	0	60	20	20JUN05	18JUL05	10OCT05	SPEC
1100	ShpDwg-PRE FAB METAL BUILDING	0	3	20	20JUN05	18JUL05	21JUL05	STEEL
1110	ShpDwg-METAL FABRICATIONS	0	3	20	20JUN05	18JUL05	21JUL05	STEEL
1210	ShpDwg-DOORS/FRAMES/HARDWARE	0	21	20	20JUN05	18JUL05	16AUG05	DOOR
1270	ShpDwg-TILE	0	62	20	20JUN05	18JUL05	12OCT05	TILEC
1280	ShpDwg-ACOUSTICAL CEILINGS	0	49	20	20JUN05	18JUL05	23SEP05	GYP
1310	ShpDwg-PAINTING	0	41	20	20JUN05	18JUL05	13SEP05	PAINT
1320	ShpDwg-WALLCOVERING	0	41	20	20JUN05	18JUL05	13SEP05	PAINT
1340	ShpDwg-TOILET COMPARTMENTS	0	7	20	20JUN05	18JUL05	27JUL05	SPEC2
1350	ShpDwg-LOUVERS/VENTS	0	8	20	20JUN05	18JUL05	28JUL05	LOCK
1380	ShpDwg-SIGNS	0	22	20	20JUN05	18JUL05	17AUG05	GEN
1400	ShpDwg-FIRE EXTINGUISHERS/ACCESSORIES	0	44	20	20JUN05	18JUL05	16SEP05	FIRE
1420	ShpDwg-TOILET/BATH ACCESSORIES	0	9	20	20JUN05	18JUL05	29JUL05	SPEC2
1490	ShpDwg-MECHANICAL-HVAC EQUIPMENT	0	0	20	20JUN05	18JUL05	18JUL05	MECH
1520	ShpDwg-MECH-FANS,CURBS	0	34	20	20JUN05	18JUL05	02SEP05	MECH
1530	ShpDwg-MECHANICAL-AIR DISTRIBUTION	0	0	20	20JUN05	18JUL05	18JUL05	MECH
1550	ShpDwg-MECHANICAL-CONTROLS	0	0	20	20JUN05	18JUL05	18JUL05	MECH
1560	ShpDwg-FIRE SPRINKLERS	0	44	20	20JUN05	18JUL05	16SEP05	FIRE
1570	ShpDwg-ELECTRICAL-RACEWAYS	0	40	20	20JUN05	18JUL05	12SEP05	ELEC
1580	ShpDwg-ELECTRICAL-WIRES/CABLES	0	40	20	20JUN05	18JUL05	12SEP05	ELEC
1590	ShpDwg-ELECTRICAL-BOXES/FITTINGS	0	40	20	20JUN05	18JUL05	12SEP05	ELEC
1600	ShpDwg-ELECTRICAL-WIRING DEVICES	0	40	20	20JUN05	18JUL05	12SEP05	ELEC
1610	ShpDwg-ELECTRICAL-DISCONNECTS	0	40	20	20JUN05	18JUL05	12SEP05	ELEC
1640	ShpDwg-ELECTRICAL-PANELBOARDS	0	0	20	20JUN05	18JUL05	18JUL05	ELEC
1650	ShpDwg-ELECTRICAL-FUSES	0	0	20	20JUN05	18JUL05	18JUL05	ELEC
1660	ShpDwg-ELECTRICAL-MOTOR STARTERS	0	0	20	20JUN05	18JUL05	18JUL05	ELEC
1670	ShpDwg-ELECTRICAL-LIGHT FIXTURES	0	0	20	20JUN05	18JUL05	18JUL05	ELEC
1800	ShpDwg-RESTEEL/ANCHOR BOLT SHP DRWG	0	30	20	20JUN05	18JUL05	29AUG05	RESTE
1260	ShpDwg-GYPSUM BOARD SYSTEMS	0	0	20	05JUL05	01AUG05	01AUG05	GYP

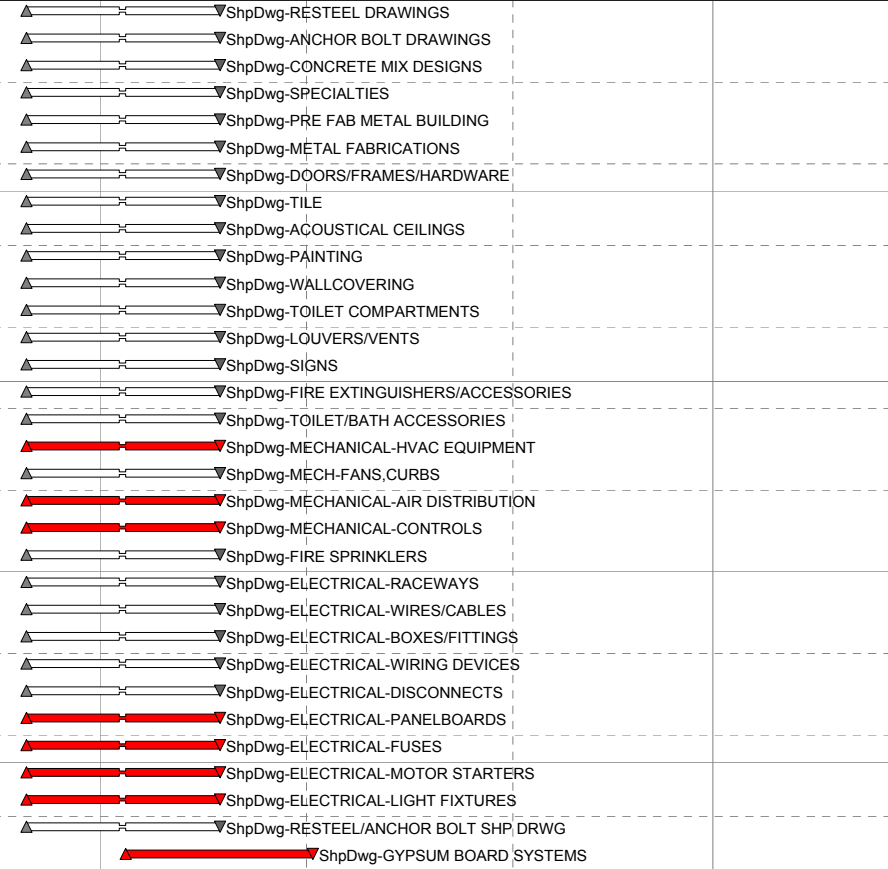


## Procurement Fab/Delivery

### Fabrication/Delivery

1115	Fab-Structural Steel	0	3	6	19JUL05	26JUL05	29JUL05	STEEL
1118	Fab-Resteel	0	30	32	19JUL05	31AUG05	12OCT05	RESTE
1215	Fab-Doors/Frames/Hardware	0	21	35	19JUL05	05SEP05	04OCT05	DOOR
1345	Fab-Toilet Compartments	0	7	50	19JUL05	26SEP05	05OCT05	SPEC2
1355	Fab-Louvers/Vents	0	8	40	19JUL05	12SEP05	22SEP05	MECH
1385	Fab-Signs	0	22	40	19JUL05	12SEP05	12OCT05	GEN
1425	Fab- Toilet/Bath Accessories	0	9	50	19JUL05	26SEP05	07OCT05	SPEC2
1495	Fab-HVAC Equipment	0	0	59	19JUL05	07OCT05	07OCT05	MECH
1525	Fab-Fans, Curbs, ETC.	0	34	25	19JUL05	22AUG05	07OCT05	MECH



Start Date	06JUN05
Finish Date	14OCT05
Data Date	06JUN05
Run Date	26MAR05 05:15




DCE2  
 Various Locations  
 MATOC DC  
 Sol: W912R1-05-R-002 Exhibit E-2

Sheet 1 of 2

Date	Revision	Checked	Approved

Activity ID	Activity Description	% Comp	Total Float	Orig Dur	Early Start	Early Finish	Late Finish	RESP
1565	Fire Marshal Review	0	44	20	19JUL05	15AUG05	14OCT05	FIRE
1665	Fab-Pnlbrds, fuses, motor starters	0	0	40	19JUL05	12SEP05	12SEP05	ELEC
1675	Fab-Light Fixtures	0	0	54	19JUL05	30SEP05	30SEP05	ELEC



**CONSTRUCTION PHASE: E-2: REPAIR HVAC & CEILING**

GENERAL/ADMIN								
1790	AllPhase-Award Project Start	0	0	0	06JUN05			GEN
1890	AllPhase-Stamped Plans	0	0	10	06JUN05	17JUN05	17JUN05	GEN
1940	AllPhase-Permits/Fees/Notices	0	0	10	06JUN05	17JUN05	17JUN05	GEN
2440	AllPhase-Notice to Proceed	0	0	0	20JUN05			GEN
2490	AllPhase-Mobilize	0	16	2	20JUN05	21JUN05	14JUL05	GEN
2504	AllPhase-Bond/Insur./CPM/Shop Dwgs	0	17	1	20JUN05	20JUN05	14JUL05	GEN
2590	AllPhase-Layout	0	13	5	20JUN05	24JUN05	14JUL05	GEN
CLOSEOUT	AllPhase-Project Closeout	0	0	1	14OCT05	14OCT05	14OCT05	GEN
THEEND	AllPhase-PROJECT COMPLETION	0	0	0		14OCT05	14OCT05	GEN




**E-2: REPAIR HVAC AND CEILING - BLDG 3109**

MAIN STRUCTURE								
P111310	Main Build-Start	0	13	0	27JUN05			GEN
P111316	Main Build-Mechanical Demolition	0	14	10	27JUN05	11JUL05	29JUL05	MECH
P111317	Main Build-Electrical Demolition	0	14	10	27JUN05	11JUL05	29JUL05	ELEC
P111300	Main Build-General Demolition	0	13	10	29JUN05	13JUL05	01AUG05	GEN
P111428	Main Build-Structural Steel	0	3	4	27JUL05	01AUG05	04AUG05	STEEL
P111396	Main Build-Metal Studs	0	0	3	02AUG05	04AUG05	04AUG05	GYP
P111232	Main Build-Carpentry/Blocking	0	44	5	05AUG05	11AUG05	12OCT05	GEN
P111330	Main Build-Gypsum Board	0	18	10	05AUG05	18AUG05	13SEP05	GYP
P111370	Main Build-Mechanical RI	0	0	35	05AUG05	22SEP05	22SEP05	MECH
P111446	Main Build-Wall Covering/Paint	0	18	7	19AUG05	29AUG05	22SEP05	PAINT
P111236	Main Build-Ceiling Grid	0	19	5	30AUG05	05SEP05	30SEP05	GYP
P111416	Main Build-Specialties	0	30	2	30AUG05	31AUG05	12OCT05	SPEC
P111266	Main Build-Door Frames	0	21	5	06SEP05	12SEP05	11OCT05	DOOR
P111268	Main Build-Doors/Hardware	0	21	1	13SEP05	13SEP05	12OCT05	DOOR
P111278	Main Build-Electrical RI	0	0	14	13SEP05	30SEP05	30SEP05	ELEC
P111364	Main Build-Mechanical Finishes	0	0	6	23SEP05	30SEP05	30SEP05	MECH
P111442	Main Build-Toilet Accessories	0	9	3	27SEP05	29SEP05	12OCT05	SPEC2
P111444	Main Build-Toilet Partitions	0	7	5	27SEP05	03OCT05	12OCT05	SPEC2
P111238	Main Build-Ceiling Tile	0	0	3	03OCT05	05OCT05	05OCT05	GYP
P111270	Main Build-Electrical Finishes	0	0	3	03OCT05	05OCT05	05OCT05	ELEC
P111365	Main Build-Mechanical Test & Balance	0	0	5	06OCT05	12OCT05	12OCT05	MECH
P111358	Main Build-Mechanical Equipment	0	0	3	10OCT05	12OCT05	12OCT05	MECH
P111412	Main Build-Punchlist	0	0	1	13OCT05	13OCT05	13OCT05	



Start Date 06JUN05  
 Finish Date 14OCT05  
 Data Date 06JUN05  
 Run Date 26MAR05 05:15



DCE2  
**Various Locations**  
 Sheet 2 of 2  
**MATOC DC**  
 Sol: W912R1-05-R-002 Exhibit E-2

Date	Revision	Checked	Approved
